

Statement of Work
for Transformational Services
Intelligent Email Triage and Response
SOW - UC - 10(2026-03)


Scope


Vendor will design, build and test in the development environment set forth herein in the Implementation Plan and subsequently deploy in the pre-production environment defined in the Implementation plan, an AI-powered solution for Investor Services that will ingest emails and attached documents as required, categorize them and assign them to appropriate tasks and owners for subsequent downstream action. Investor Services receives 80,000 - 100,000 emails per month from investors/clients for onboarding, maintenance, reporting, inquiries and ongoing communications & reporting. Currently, the emails are manually reviewed, categorized, triaged and assigned to appropriate stakeholders manually. The solution will interface with the IS client inboxes and perform bulk of the human actions in terms of reviewing, prioritizing and assigning actions to appropriate stakeholders/teams. The solution will also have a mechanism to measure the efficacy of the automation for email triage and learn based on corrections made to the email assignment and triage as described in Appendix A to this schedule 1.

In addition, the automation will leverage information from JIRA that is logged by task assignees to support automation of client responses/communications to request for clarifications, missing information or communication of task outcome to clients. The key assumption here is that the commentary in JIRA will be adequately updated by task assignees. The automation will also provide a summarized view (by client) highlighting the number of requests, the number of requests by task type and trends.

For the purposes of this SOW, the scope will be focused on processes performed in the US. Dublin processes will be picked up as a Change Request (CR) as required. The scope includes email triage and automation of client responses/communications and does not include the actual execution of the activities required in the email.

Below are initial views of Current State and Target State processes for email triage.

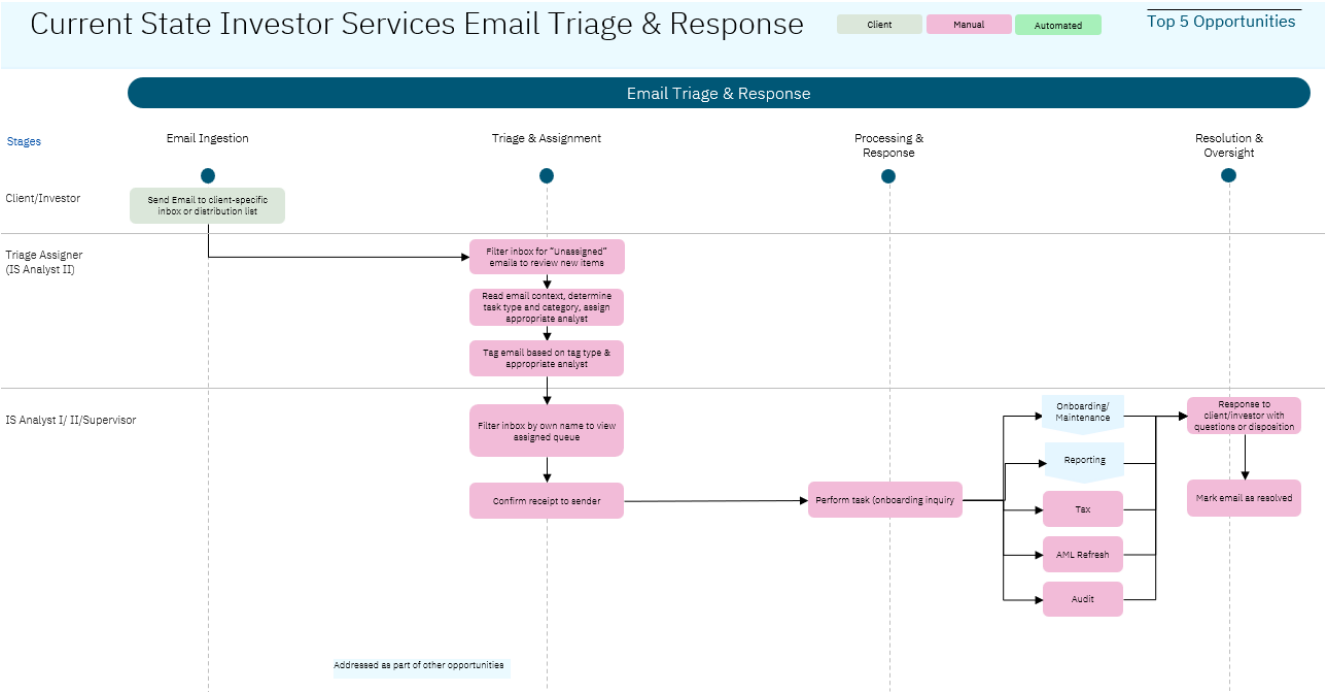

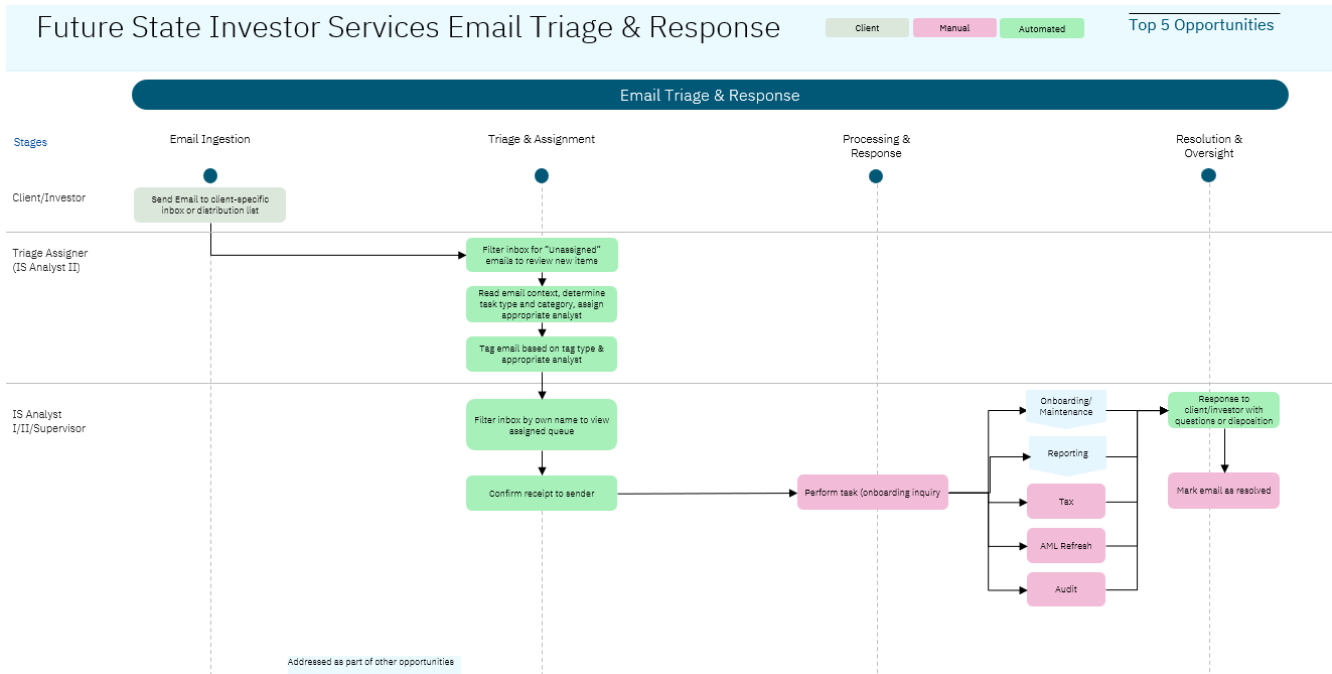


Agent Flow Architecture:

UC10: Use Case Architecture

Email Triage & Response Automation/ Workflow Orchestration

Architecture Narrative: The platform requirements include (1) multiple email boxes, (2) an agent that monitors those boxes and captures the content into a normalized format, (3) an agent that reads the content and determines where to route the email - this agent is grounded in an application context built of previous routed examples, (4) a validator agent that checks the work of the first agent with a different model, (5) an agent that routes the email to Jira, (6) an agent that monitors activity in Jira and auto-learns, improving the application context for the next set of emails.


Archetype
General Pro-Code AI Agent

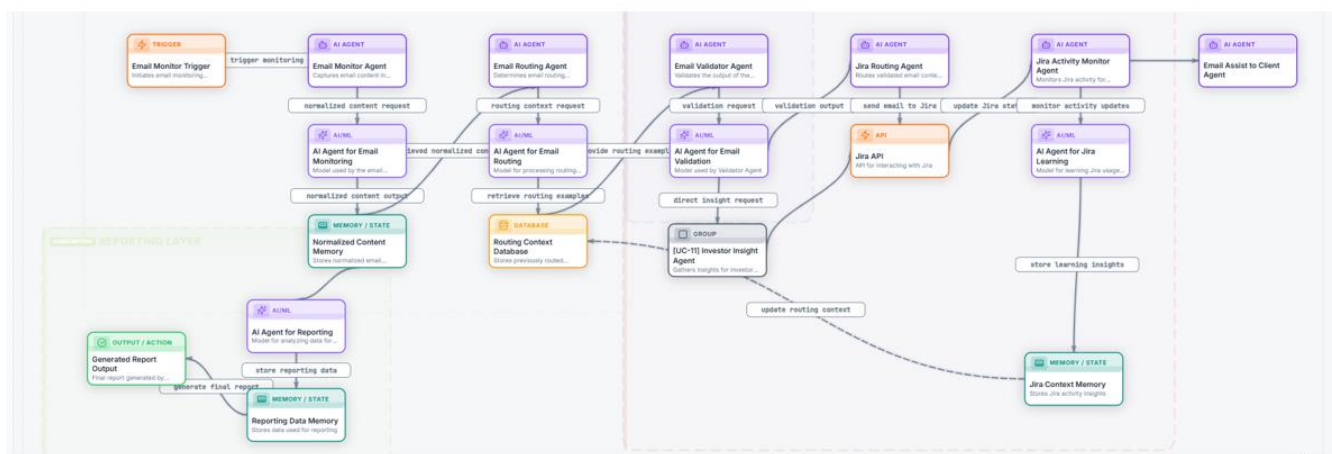

Physical Architecture:

The solution will be built within SEI's Microsoft Azure environment. The solution will not communicate outside SEI's environment, and the data is entirely private to SEI. IBM and SEI will agree on a final version of the architecture after completion of design planning.

#1335948v8

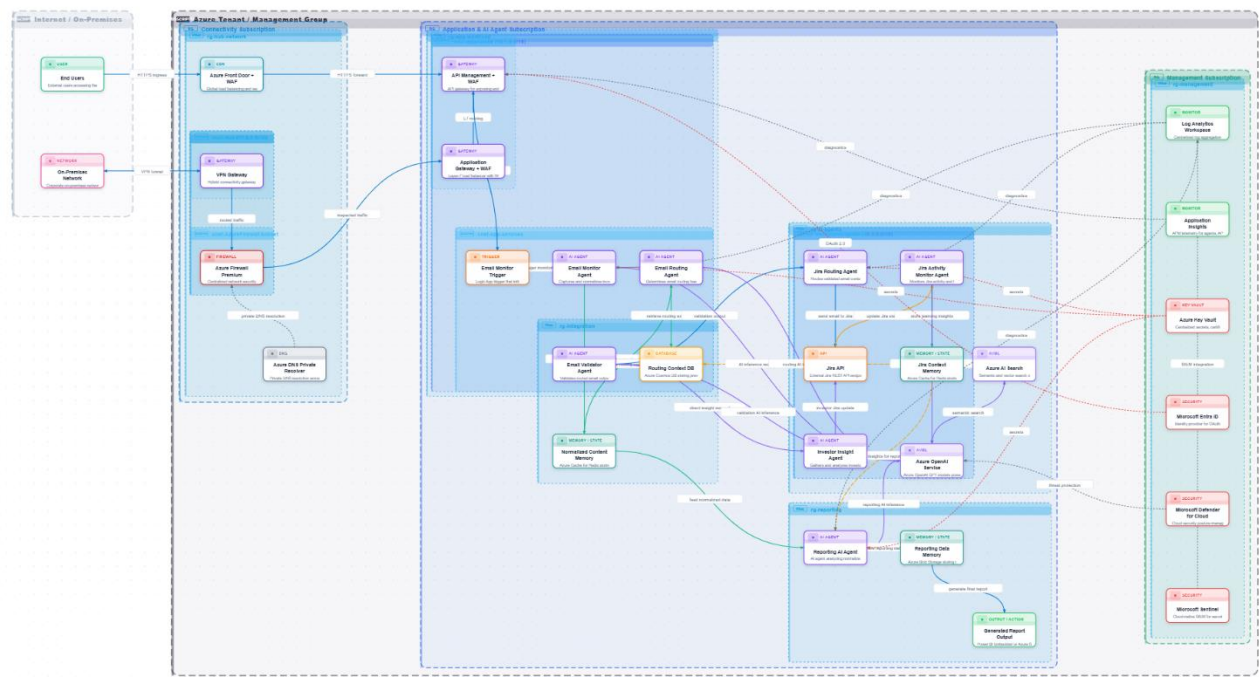

Category	Component	Requirement / Description
Application Layer	Azure App Service	Hosts web UI and REST APIs (if required)
	REST APIs	Enables integration with external and internal systems
	UI (Composer)	Used for configuration, monitoring, and human review
Compute & Orchestration	Azure Container Apps	Runs DocuFlow backend and multi-agent orchestration
	Azure Function Apps	Executes modular processing and integrations
	Agent Framework	Coordinates extraction, validation, and business rule agents
Data & Storage	Azure Blob Storage	Stores raw documents, outputs, and intermediate files
	Azure Storage Accounts	Supports orchestration state, logs, and training datasets
	Cosmos DB (Mongo API)	Stores prompts, configuration, and ontology definitions
	Azure AI Search (Vector DB)	Provides long-term memory and semantic search over documents
AI Services	Azure Document Intelligence	OCR, layout extraction, prebuilt document models
	Azure OpenAI	Extraction, enrichment, validation, and formatting using LLMs
	Foundry Agents	Runs scaled agents on demand
Security & Governance	Identity & Access	Azure Entra ID (RBAC) for user and system access
	Compliance	Azure Policy for governance and regulatory enforcement
	Auditability	Tracks corrections, validation, and processing actions
Resiliency	High Availability	Multi-region failover and resilient processing pipeline
	Data Persistence	Stores intermediate states and logs for recovery
Deployment	Environments	Dev, Test/UAT, Prod with isolated resources
	Platform Model	Azure PaaS-based, scalable, event-driven architecture
	DevOps	GitHub (or other repo platform)

Vendor shall prepare and deliver the following documents:

- 1. **Analysis Documentation** – User stories in templates aligned with SEI
- 2. **Solution Design Artifacts** – Detailed solution architecture in templates aligned with SEI
- 3. **Test Documentation** – Test approach, test case and test data related documentation in templates aligned with SEI
- 4. **Solution Deployment Documentation** - Deployment Documentation in templates aligned with SEI
- 5. **Operational Documentation** – NA; Any updates to existing procedural documentation and change management related documentation will be handled by SEI

Pre-Production Delivery:

Pre-Production Environment: The environment to perform UAT for the email triage and response process and will be identified during deployment. This will be environment where the code/automation will be moved, the systems of record validated for updates and sample emails triaged and responses validated/processed by the client.

Acceptance Test:

The UAT will be performed with the goal of measuring and validating 2 key criteria for the outputs:

Reduction in processing time through automation Acceptance Criteria for each Deliverable:

- 1. Processing time reduction of 25% or higher

Production Delivery:

Dependencies and SEI Internal Requirements

1. *Dependencies*

Dependency	Internal Stakeholder	Responsible Party	Estimated Time Period

2. *SEI Internal Requirements and Expected Timing*

Internal Process	Internal Stakeholder	Responsible Party	Estimated Time Period
Change Management including Procedure updates	Brad Landis	Rob Bonanno	Prior to Ph I deployment
Infrastructure set-up for development, UAT and production environments to build and deploy automations	Brad Landis	Zach Womack	Prior to commencement of respective project phases
Access to Outlook, JIRA	Brad Landis	Zach Womack	Prior to 5/22

Schedule 2

Fees

1. Constant Costs

The parties agree the following costs have been validated for calculation of both the SOW Transformation Value and the Gainshare Fees:

a. Annual In-Scope Constant Cost/FTE

Role	US
IS Analyst I	\$ 62,000
IS Analyst II	\$ 68,000
IS Supervisor	\$ 85,000
IS Assistant Manager	\$ 100,000
Manager	\$ 119,000

b. Current Total In-Scope US Annual Spend (Including Email Triage and Email Responses/Communications to Clients):

Total – Email Triage and Responses/Communications:

Role	Annual FTE Capacity (US)	Average Cost US	Total Cost
IS Analyst I	4.5	\$ 62,000	\$ 276,383
IS Analyst II	6.9	\$ 68,000	\$ 465,922
IS Supervisor	5.5	\$ 85,000	\$ 467,291
IS Assistant Manager	3.7	\$ 100,000	\$ 366,503
IS Manager (10% of other resource effort)	2.8	\$ 119,000	\$ 331,062
Total	23.3		\$ 1,907,161

Email Triage: (20% of Total capacity ~ 30 seconds per email in Current State)

Role	Annual FTE Capacity (US)	Average Cost US	Total Cost
IS Analyst I	0.9	\$ 62,000	\$ 55,277
IS Analyst II	1.4	\$ 68,000	\$ 93,184
IS Supervisor	1.1	\$ 85,000	\$ 93,458
IS Assistant Manager	0.7	\$ 100,000	\$ 73,301
IS Manager (10% of other resource effort)	0.6	\$ 119,000	\$ 66,212
Total	4.7		\$ 381,432

Email Communications/Responses: (80% of Total capacity)

Role	Annual FTE Capacity (US)	Average Cost US	Total Cost
IS Analyst I	3.6	\$ 62,000	\$ 221,106
IS Analyst II	5.5	\$ 68,000	\$ 372,737
IS Supervisor	4.4	\$ 85,000	\$ 373,833
IS Assistant Manager	2.9	\$ 100,000	\$ 293,202
IS Manager (10% of other resource effort)	2.2	\$ 119,000	\$ 264,850

Total	18.6		\$ 1,525,729
-------	------	--	--------------

- c. Total Value Creation
 - i) Increased Efficiency (reduction in processing time):
 - a. **Email Triage:** Expected processing time reduction of 75%.
 - b. **Email Responses/Communications:** Expected processing time reduction of 60%.
 - c. **Reporting:** Summary monthly report for each client highlighting the number of requests, number of request types and trends month over month

2. SEI Internal Enablement Costs

The parties hereby agree that the internal SEI resource commitments and third-party expenditure required to procure under this SOW are expected to be a total of \$52,000 which includes the following components:

- Annual Technology and Infrastructure Cost - \$52,000 which includes but not limited to the following components:
 - 1. Azure Foundry Agents
 - 2. LLM Tokens
 - 3. Container Apps
 - 4. Storage (Blob and RDB)

3. SOW Transformation Value Calculation Methodology

For the purposes of this SOW, the following terms shall have the following meanings:

“Total Annual Spend Reduction” shall mean the Current Total In-Scope Annual Spend less the End State Total In-Scope Annual Spend set forth in Schedule 3.

“SOW Transformation Value “- The Total Annual Spend Reduction plus the Total Value Creation less the SEI Enablement Costs set forth below.

“End State Annual Spend” – means the sum of (the On-Shore Target In-Scope FTE for each Role set forth in Schedule 3 multiplied by the On-Shore Total In-Scope Annual Constant Cost/FTE for the applicable role) plus the sum of (the Off-Shore Target In-Scope FTE by Role set forth in Schedule 3 multiplied by the Off-Shore Total In-Scope Annual Constant Cost/FTE for the applicable role.

“SOW Transformation Value “- The Total Annual Spend Reduction plus the Total Value Creation less the SEI Enablement Costs set forth below.

4. SOW Transformation Value

The parties hereby agree the Transformation Value for this SOW is \$1,149,512 (the “**SOW Transformation Value**”).

SOW Value Creation	\$ 1,201,512
SEI Internal Enablement Costs (12 months)	\$52,000
SOW Transformation Value	\$1,149,512

5. Gainshare Fees

SEI hereby agrees to pay Vendor fees (the “Gainshare Fees”) estimated at \$344,853 for, and Vendor agrees to perform, the Services set forth in Schedule 1. The estimated Gainshare Fees are calculated at 30% of the SOW

#1335948v8

Transformation Value for all phases listed in Section 4. Transformation Value and Gainshare Fees will be memorialized at Delivery Completion milestone and 70% of the Gainshare Fees will be paid to Vendor (“Initial Fee”). Actual Transformation value and Gainshare Fees will be memorialized at Validation milestone to reflect actual SOW Transformation Value and any remaining Gainshare Fees will be paid to the vendor (“Remaining Fee”).

		Estimated Transformation Value	Demonstrated at Delivery Completion Milestone	Actual at Validation Milestone
Triage	Transformation Value	\$ 275,675	TBC	TBC
	Gainshare Fees	\$ 82,702	TBC	TBC
Response & Communications	Transformation Value	\$ 873,837	TBC	TBC
	Gainshare Fees	\$ 262,151	TBC	TBC
Total	Transformation Value	\$ 1,149,512	TBC	TBC
	Gainshare Fees	\$ 344,853	TBC	TBC

6. Payment Schedule

The parties agree that the Gainshare Fees shall be paid based on the payment schedule found in the table below:

	Estimated Initial Fee	Anticipated Payment date	Estimated Remaining Fee	Anticipated Payment date
Triage	\$57,892	9/4/2026	\$24,810	12/4/2026
Response & Communications	\$183,506	9/25/2026	\$78,645	12/23/2026
TOTAL	\$ 241,398		\$103,455	

The deployment will follow a 2-phased approach

- Phase 1 – Email triage automation rollout to all clients
- Phase 2 – Response and Communications creation rollout to all clients

Schedule 3

Measurement Metrics and Acceptance Testing

Measurement Metrics and Acceptance Criteria

The parties hereby agree that the following metrics will be the applicable measurement metrics (the “**Measurement Metrics**”) for measurement purposes and demonstration that the Deliverable achieves the Target Measurement Metrics (as defined below) shall constitute the acceptance criteria and the criteria for Validation (the “**Acceptance Criteria**”). For the purposes of this SOW UC-10, “Onshore” shall mean the US and “Offshore” shall mean India.

Measurement Metrics

Processing Time – The amount of time spent performing the In-Scope Process in current state vs future state.

Baseline Measurement Metrics – Email Triage

The parties agree the following Measurement Metrics have been agreed and validated as the Baseline Measurement Metrics and will be the basis for calculation of both the SOW Transformation Value and the Gainshare Fees:

- a. The Total current monthly volume of incoming emails = 80,000 – 100,000
- b. Total annual US FTE capacity spent = 4.7
- c. Average volume triaged per day = 4,000 – 5,000
- d. Current triaging time for ~2500 emails = 4.4 hours (2500 emails triaged at 30 sec/email by 4.7 resource capacity)

Target Measurement Metrics – Email Triage

- a. Target triaging time for ~ 2500 emails (at 75% Transformation) = 1.1 hour

Testing Criteria/ Methodology – Email Triage

The parties hereby agree that for the purpose of the Measurement Metrics for calculation of BAU Measurement Metrics and Acceptance Testing, the following testing parameters shall apply:

Sample Criteria

1. Sample size – 2500 emails
2. Samples will include different examples of emails from clients representative of the Production environment
3. Ability to validate all input channels (emails, JIRA)
4. JIRA test environments available to validate E2E workflow (as required)

Quality Testing - Email Triage

1. The output of the email triage automation identifies tasks accurately and tags to the appropriate users

Processing Time testing – Email Triage

1. Initial enablement of users to interact with the automation at a comfortable level
2. 5 rounds of testing will be performed (average of 500 emails each round) – average processing time will be calculated based on the time taken to execute the testing with IBM being side by side with SEI

3. Triaging time will be calculated based on time taken for emails triaged accurately + additional effort required to manually re-route emails triaged inaccurately (at 30 seconds per email)

Baseline Measurement Metrics – Email Responses

The parties agree the following Measurement Metrics have been agreed and validated as the Baseline Measurement Metrics and will be the basis for calculation of both the SOW Transformation Value and the Gainshare Fees:

- a. Total annual US FTE capacity spent = 18.6
- b. Total volume of email responses to clients (including clarification emails and final communications emails) – Unknown

Target Measurement Metrics – Email Responses

- a. Target FTE capacity to handle current volume = 7.4 (at 60% Transformation)

Testing Criteria/ Methodology – Email Responses

The parties hereby agree that for the purpose of the Measurement Metrics for calculation of BAU Measurement Metrics and Acceptance Testing, the following testing parameters shall apply:
Sample Criteria

1. Sample size – Create 100 Email Communications from 100 JIRA requests
2. Types of email communications created will include documentation requests, clarifying questions, final disposition etc. in proportions representative of the Production environment
3. Outlook and JIRA test environments available to validate E2E workflow (as required)

Quality Testing - Email Responses

1. The output of the email response automation gathers context adequately from JIRA with appropriate content to reduce effort required to send emails.

Processing Time testing – Email Responses

1. Initial enablement of users to interact with the automation at a comfortable level
2. 4 rounds of testing will be performed (average of 25 emails each round)
 - i) Average processing time (pre-automation) will be measured based on the time taken to send required emails to clients (IBM being side by side with SEI)
 - ii) Average processing time (post-automation) will be calculated based on time taken to send required emails to clients for the same emails review in pre-automation (i) step above with IBM being side by side with SEI.

Schedule 4

Termination Rights and Fees

In the event SEI elects to terminate this SOW, in whole or in part, for convenience before the end of the Term, SEI shall pay Vendor \$ 115,000.

Schedule 5


Technology Tools and Existing IP

- 1.** Pre-Existing IP:
 - a. SEI: None
 - b. Vendor: None

Appendix A

Implementation Plan (the “Implementation Plan”)

The approvals and related controls for steps listed in the Implementation Plan will be aligned during Kick-off with SEI

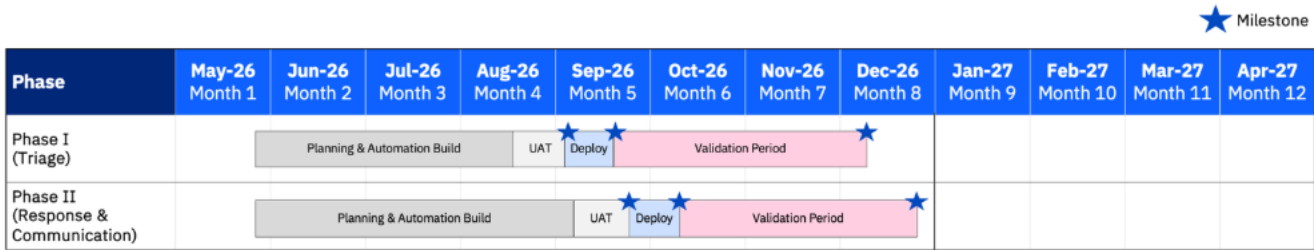

Email Triage

Step	Period/Scheduled Completion Date	Owner
Triage + Reporting - User Stories completion	5/29/2026	IBM
Triage + Reporting - Solution Design documentation and validation	6/5/2026	IBM
Triage + Reporting - Test Approach, Test Data and Test Case Completion for all phases	6/12/2026	IBM
Triage + Reporting - Build and Configure	8/21/2026	IBM
Triage + Reporting - Move to Pre-Production	8/21/2026	IBM
Triage + Reporting - UAT Completion	9/4/2026	IBM / SEI
Triage + Reporting - Production Change Control	9/11/2026	SEI
Triage + Reporting - Production Deployment	9/11/2026	SEI
Triage + Reporting - Hypercare/Post-Implementation Support	9/25/2026	IBM
Triage Ph I - Validation Period	12/4/2026	SEI

Email Response & Communications:

#1335948v8

Step	Period/Scheduled Completion Date	Owner
Response & Communications - User Stories completion	5/29/2026	IBM
Response & Communications - Solution Design documentation and validation	6/5/2026	IBM
Response & Communications - Test Approach, Test Data and Test Case Completion for all phases	6/19/2026	IBM
Response & Communications - Build and Configure	9/11/2026	IBM
Response & Communications - Move to Pre-Production	9/11/2026	IBM
Response & Communications - UAT Completion	9/25/2026	IBM / SEI
Response & Communications - Production Change Control	10/2/2026	SEI
Response & Communications - Production Deployment	10/2/2026	SEI
Response & Communications - Hypercare/Post-Implementation Support	10/16/2026	IBM
Response & Communications - Validation Period	12/23/2026	SEI

Sample Documentation Request Requirements:

SEI will use commercially reasonable efforts to provide sample data according to the requirements and timelines mentioned in the table below, for Vendor to be able to adequately perform the anticipated Build and Configure activities in the Implementation Plan. The sample documentation will be scrubbed of all personally identifiable information according to SEI requirements.

Category	Subcategory	Client	Date Required for 2 Examples	Date Required for 5 Examples
Account Maintenance	Address Change	Client A	6/30/26	7/17/26
		Client B	6/30/26	7/17/26
		Client C	6/30/26	7/17/26
	AML Affiliated Related Party Update	Client A	6/30/26	7/17/26
		Client B	6/30/26	7/17/26
		Client C	6/30/26	7/17/26
	Authorized Signer Changes	Client A	6/30/26	7/17/26
		Client B	6/30/26	7/17/26
		Client C	6/30/26	7/17/26
	Contact Update	Client A	6/30/26	7/17/26
		Client B	6/30/26	7/17/26
		Client C	6/30/26	7/17/26
	Custodian Account Number Change	Client A	6/30/26	7/17/26
		Client B	6/30/26	7/17/26
		Client C	6/30/26	7/17/26
	Custodian Change	Client A	6/30/26	7/17/26
		Client B	6/30/26	7/17/26
		Client C	6/30/26	7/17/26
	ERISA Status Change	Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26
	FINRA 5130 Restricted Status Change	Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26
	FINRA 5131 Restricted Status Change	Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26
	Distribution Election Change	Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26
	Name Change	Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26

		Wire Instruction Change	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26
			Client C	7/10/26	7/24/26
		Other	Client A	7/17/26	7/24/26
			Client C	7/17/26	7/24/26
			Client B	7/17/26	7/24/26
Tax		n/a	Client A	7/6/26	7/17/26
			Client C	7/6/26	7/17/26
			Client B	7/6/26	7/17/26
AML		n/a	Client A	7/6/26	7/17/26
			Client C	7/6/26	7/17/26
			Client B	7/6/26	7/17/26
Audit Confirmations		n/a	Client A	7/6/26	7/17/26
			Client C	7/6/26	7/17/26
			Client B	7/6/26	7/17/26
Investor Inquiries		n/a	Client A	7/6/26	7/17/26
			Client C	7/6/26	7/17/26
			Client B	7/6/26	7/17/26
Wires		n/a	Client A	7/6/26	7/17/26
			Client C	7/6/26	7/17/26
			Client B	7/6/26	7/17/26
Client Inquiries		n/a	Client A	7/6/26	7/17/26
			Client C	7/6/26	7/17/26
			Client B	7/6/26	7/17/26
Onboarding		New Subscription	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26
			Client C	7/10/26	7/24/26
		Additional Subscription	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26
			Client C	7/10/26	7/24/26
		New Commitment	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26
			Client C	7/10/26	7/24/26
		Additional Commitment	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26
			Client C	7/10/26	7/24/26
		Full Transfer	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26
			Client C	7/10/26	7/24/26
		Partial Transfer	Client A	7/10/26	7/24/26
			Client B	7/10/26	7/24/26

Non-Actionable/Suppress	Full Switch or Exchange	Client C	7/10/26	7/24/26
		Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26
	Partial Switch or Exchange	Client A	7/10/26	7/24/26
		Client B	7/10/26	7/24/26
		Client C	7/10/26	7/24/26
	n/a	Client A	7/17/26	7/24/26
		Client C	7/17/26	7/24/26
		Client B	7/17/26	7/24/26
