

STATEMENT OF WORK-----STATEMENT OF WORK
FOR TRANSFORMATIONAL SERVICES
INTELLIGENT FEE CALCULATION

SOW – UC 19 (2026 - 02)

This STATEMENT OF WORK FOR SERVICES (this “**INTELLIGENT FEE CALCULATION SOW**”), is entered into as of July 2, 2026 (“**SOW Effective Date**”) by and between SEI Global Services Inc. (“**SEI**”) and International Business Machines Corporation (“**Vendor**”), pursuant to the Master Statement of Work For Transformational Services, dated as of April 15, 2026 by and between SEI and Vendor (the “**MSOW**”) pursuant to the Master Agreement, effective as of March 18, 2026, by and between SEI and Vendor (the “**MSA**”). For the purposes of this “**INTELLIGENT FEE CALCULATION SOW**”, the term SOW shall mean the MSA, together with the MSOW and this **INTELLIGENT FEE CALCULATION SOW**, but not other SOWs entered into under the MSA or MSOW (this “**SOW**”). Capitalized terms not defined in this **INTELLIGENT FEE CALCULATION SOW** have the meanings ascribed to them in the MSOW or the MSA, as applicable.

VENDOR CONTACT:	Manoj Sthanu
TELEPHONE:	+1-201 565 6854
EMAIL:	Manoj.Sthanu@ibm.com

Changes to this SOW will be processed as a Change Order as set forth in the MSOW. The implementation of changes may result in modifications to the Estimated Schedule, Charges, and other terms of this SOW, which will be agreed by the parties and documented in a Change Order.

The following are incorporated in and made part of this SOW:

- Schedule 1: Scope of Services, and any Deliverables
- Schedule 2: Fees
- Schedule 3: Measurement Metrics
- Schedule 4: Termination Rights and Fees
- [Schedule 5 Technology Tools and Existing IP]
- Appendix A: Implementation Plan (the “Implementation Plan”)

1. **Term.** The initial term of this SOW begins on the SOW Effective Date and ends on May 31, 2027, unless terminated earlier in accordance with the terms of the Agreement (the “**SOW Initial Term**”).

2. **Services.**

- a. **Scope.** Vendor will perform the Services set forth in Schedule 1 attached hereto (the “**Services**”), In accordance with the terms and conditions of the Agreement, MSOW and this SOW.

Solution and Technical Dependency Summary: The Solution will extract fee basis data systematically from Geneva/InvesTran/InvesTier reports into investor-level fee calculation engine eliminating manual population of templates, and will perform QC checks with transparency for user validation and approval, will integrate waterfall calculations in Anaplan, will automate uploaders to accounting engines and deliver to existing client servicing interfaces where clients can access fee calculation data.

- b. **No Investor Advisor Functions.** SEI and Vendor agree that Vendor will not perform, and none of the Services involve the performance of, investor advisor functions on behalf of SEI

- c. **Language Requirements.** Vendor will perform the Services in the English language.

3. **Pre-Production Delivery; Deliverables and Delivery Completion Criteria.** For each phase, Vendor will deliver the applicable Deliverable into the Pre-Production Environment (as defined in Schedule 1) provided by SEI (“**Delivery**”). Following such Delivery, SEI shall have a set number of business days by phase according to the table below (unless otherwise aligned with the Vendor), from the date of such Delivery (the “**Acceptance Period**”) to review the Deliverable and validate the Deliverable satisfies the applicable Acceptance Criteria in accordance with Schedule 1 of this SOW (“**Acceptance Testing**”) and either 1) provide Vendor with notice of any Non-Conformities, along with a specific description of such Non-Conformities (“**Non-Conformity Notice**”) or 2) provide

Vendor with written notice of Delivery Completion. If Vendor receives a Non-Conformity Notice prior to the end of the Acceptance Period, Vendor shall comply with the remediation process outlined in Section 4.1 of the MSOW.

Phase	Description	UAT Duration
Phase 1	Golden Data Set for Fee Calculation and Management Fee Automation for Top 10 Clients	15 Business Days
Phase 2	Extend Management Fee Automation and Deliver Carried Interest Calculation Automation	20 Business Days
Phase 3	Incentive and Administrative Fee Automation, Workflow and Dashboard	20 Business Days

4. **Deployment in Production; Dependencies and Internal Requirements.** Upon Delivery Completion for each phase, the parties will satisfy their respective conditions and dependencies for such phase as set out in Schedule 1 attached hereto (the “**Dependencies**”). In addition, Schedule 1 of this SOW sets forth SEI's Internal Requirements for this SOW. Planned releases will be aligned to dependent SEI schedule. Upon completion of the Dependencies and Internal Requirements, the parties will work to deploy the Deliverable(s) in production with a projected date of Opportunity Go-Live currently being:

Phase	Description	Estimated Opportunity Go-Live Date
Phase 1	Golden Data Set for Fee Calculation and Management Fee Automation for Top 10 Clients	September 11, 2026
Phase 2	Extend Management Fee Automation and Deliver Carried Interest Calculation Automation	November 20, 2026
Phase 3	Incentive and Administrative Fee Automation, Workflow and Dashboard	February 19, 2027

5. **Validation.** Upon the final Opportunity Go-Live, the Validation Period will commence, and the parties will confirm that the Deliverable(s) have been successfully implemented in production and meet the agreed Measurement Metrics as detailed in Schedule 3. SEI will provide written confirmation of Validation (a “**Validation Notice**”) by the last day of the Validation Period or provide Vendor with notice of any failure of the Deliverable(s) to meet the Measurement Metrics (“**Validation Shortfall Notice**”)

If SEI delivers a Validation Shortfall Notice hereunder, the process applicable to a Non-Conformity Notice and remediation under Section 3 of this SOW and Section 4.1 of the MSOW shall apply in the same manner to a Validation Shortfall Notice under this Section 5; notwithstanding the foregoing, the revalidation period under this Section 5 is 5 business days.

6. **Reports.** There are no additional reports necessary under this SOW other than the reports required for governance purposes as set forth in Section 10 of the MSOW.

7. **Service Locations.**

In accordance with Section 9.2 of the MSOW, Vendor shall provide the Services at the following locations: United States and India.

8. **Responsibilities.**

a. **Vendor Responsibilities.**

In addition to the Vendor Responsibilities set forth in the MSA and the MSOW, Vendor shall have the following additional responsibilities:

- i. Project Manager - Vendor hereby designates Nicholas Ciappa as its Project Manager for this SOW (the “**Vendor Project Manager**”) who will be the single point of contact for all communications with SEI's Project Manager. The Vendor Project Manager shall have the responsibilities set forth in the MSOW and shall provide project and operational guidance, and serve as the interface between the Vendor and any of its Approved Subcontractors participating in this SOW. The Vendor's Project Manager is a “**Key**”

Personnel". Unless otherwise agreed by the parties, all Key Personnel shall be dedicated to SEI and provide the Services described in this SOW on a full-time basis;

- ii. Vendor will conduct a knowledge transfer session and clarification session with the IMS tech and business team as part of the handoff of the solution.
- iii. Vendor assigns the following additional Key Personnel:

Vendor SOW Team	Role Description	Resource Name
Project Manager	Main point of contact	Nicholas Ciappa
Technology Architect	Primary responsibility for technology related guidance	Matthew Payne

- iv. Vendor must be experienced in the principles and regulatory implications of the financial services industry;
- v. Vendor shall adhere to the terms and conditions of this SOW and any amendments thereto; and
- vi. Vendor shall be responsible for all performance related issues, personnel reviews or rewards.

b. SEI Responsibilities.

In addition to the SEI Responsibilities set forth in the MSA and the MSOW, SEI shall have the following additional responsibilities:

- i. Project Manager – SEI hereby designates Brad Landis as its Project Manager for this SOW (the “**SEI Project Manager**”) who will be the single point of contact for all communications with Vendor’s Project Manager. The SEI Project Manager shall have the responsibilities set forth in the MSOW and shall provide project and operational guidance, and shall serve as the interface between the Vendor and all SEI Key Resources and departments participating in this SOW;
- ii. Key Resources - SEI will provide the following Key resources for SEI’s project team as set forth below.

SEI’s SOW Team	Role Description	Resource Name
Project Manager	Main point of contact	Jim Sinclair
Key Project Stakeholder	Main Business Stakeholder	Bryan Reeder
Project Technology stakeholder	Key member of the Technology Committee and Primary responsibility for technology related guidance	Michael Roy
IMS Product Stakeholder	Primary responsibility for product related guidance	Chris Jones

9. Fees.

- a. Fees. In consideration for Vendor providing the Services and Deliverables described above, SEI agrees to pay Vendor fees for the Services as set forth in Schedule 2 attached hereto (the “**Fees**”). Except as expressly stated herein, there are no additional fees, charges or expenses incurred by SEI hereunder.
- b. Fee Schedule. The Fees specified above shall become due and payable in accordance with Schedule 2 of this SOW.
- c. No Purchase Order. SEI hereby confirms and agrees that, notwithstanding the terms of this SOW, the MSOW, or our prior practice, payment under this SOW is not contingent upon issuance of a Purchase Order. All approvals required to issue payment have been obtained.

10. Technology Tools.

- a. The parties agree that the Services hereunder only involve the development or implementation of code to create the Deliverable and that the Services do not involve or require the introduction of any new technologies or tools to SEI's Systems.
- b. Pre-Existing IP. The Pre-Existing IP for each of Vendor and SEI is set forth in Schedule 5.

11. AI Tools.

This project will leverage the following foundational technology platforms available within SEI:

- Microsoft Foundry Agents
- Azure Search
- Azure Open AI endpoint
- Azure App Service

12. Impact Assessment Exercise

- a. Impact Assessment The parties hereby agree that the following events (each a “**Impact Assessment Trigger Event**”) set forth below may trigger an impact assessment exercise (an “**Impact Assessment Exercise**”) if and to the extent such event would materially and adversely impact SEI's SOW Transformation Value for the SOW, any of the Measurement Metrics or any of the Dependencies. Any party that believes a Impact Assessment Trigger Event has occurred must raise the issue at the next scheduled meeting of the Program Level Committee following such party's awareness of the alleged Impact Assessment Trigger Event, together with reasonable supporting detail. The Program-Level Steering Committee shall review the facts and circumstances and determine whether an Impact Assessment Trigger Event has occurred and, if so, whether and to what extent a recalibration is appropriate. Any failure to agree as to whether a Impact Assessment Trigger Event has occurred shall be escalated in accordance with Section 10.4 of the MSOW. Upon agreement that an Impact Assessment Trigger Event has occurred, the parties will conduct the Impact Assessment Exercise to identify the root cause of the Impact Assessment Trigger Event, determine whether any adjustments to the Implementation Plan Internal Requirements, BAU Metrics, Dependencies or assumptions are necessary or appropriate. The parties will work together, in good faith, to determine whether, after giving effect to the applicable Impact Assessment Trigger Event, any remediations or changes are necessary to the terms and conditions under this SOW, including Measurement Metrics, Implementation Plan, Opportunity Go-Live, or the Validation Period. Based upon the results of such Impact Assessment Exercise, the parties will make any necessary adjustments to Measurement Metrics, Implementation Plan or schedule, capacity expectations, fees and/or any other term, condition or assumption set forth in such SOW. The agreed-upon results of the Impact Assessment Exercise will be memorialized pursuant to a Change Order.
- b. Impact Assessment Trigger Events. The parties hereby agree that the following shall be Impact Assessment Trigger Events:
 - i. Changes to anticipated Implementation Plan that negatively impact timelines. For the avoidance of doubt, any delay or failure by SEI to provide the document set as required in the Implementation Plan shall not constitute an Impact Assessment Trigger Event.
 - ii. Any updates to the baseline metrics that reduce the SOW transformation value
 - iii. Any access or technology limitations, that negatively impact SOW transformation value

The occurrence of an Impact Assessment Trigger Event shall not, by itself, result in any automatic adjustment to the Measurement Metrics, SOW Transformation Value, fees, timelines, or other terms of the SOW.

13. Implementation Plan. The parties hereby agree that the Implementation Plan set forth in Appendix A, containing the detailed Implementation Plan and implementation schedule are applicable to the Services.

14. Termination Rights and Fees. Schedule 4 sets forth the termination rights and the related termination events and fees, including termination for convenience rights and calculation methodology for early termination amounts due.

15. Termination Assistance and Exit Rights. NA

16. Disaster Recovery/Business Continuity. The services delivered as part of this SOW are not mission critical.

Scenario	Impact	Business Continuity/Disaster Recovery Plan
Site, City outage	Schedule delay	Offshore location: Continue service using onshore resources and/or resources from back-up site in India Onshore location: IBM resources are from multiple cities; continue services using remaining onshore resources from other cities and/or resources from back-up site in India
Country outage	Schedule delay	Offshore location: Continue services using onshore resources Onshore location: Continue services using offshore resources
Unavailability of key personnel	Schedule delay	Back-up and succession plan for key personnel

17. Additional Requirements for SEI Customers. There are no additional requirements for SEI customers. Failure by Vendor to comply with any Additional SEI Requirement shall be considered a material breach of this SOW and SEI may terminate this SOW in accordance with Section 9.02(b) of the MSA.

18. No Personal Data will be processed under this SOW. Vendor will use only non-identifiable data in performing the Services (e.g., dummy test data and/or anonymized or aggregated data from which no individual can be identified). Pseudonymized data, or data that can be associated or re-associated with an individual by SEI or another party, is identifiable Personal Data and cannot be used under this subsection. Accordingly, the DPA (Data Processing Addendum) is not applicable to this SOW. If the scope of Services changes to involve any Personal Data, the parties will first execute and attach a DPA Exhibit and comply with all relevant data protection requirements before processing such data.

Each of the Parties has caused this SOW to be executed by its duly authorized representative as of the SOW Effective Date.

International Business Machines Corporation

Signed by:
By: Manoj Sthanu
2C94B906073643B...

Name: Manoj Sthanu

Title: Authorized signatory

Date: 7/2/2026

SEI Global Services, Inc.

Signed by:
By: Bradley Landis
3497F38BD7AC4A8...

Name: Bradley Landis


Title: Vice President

Date: 7/2/2026


Schedule 1

Statement of Work
for Transformational Services
Intelligent Fee Calculation
SOW – UC-19 (2026 - 02)


Scope
Vendor will design, build and test in the development environment set forth herein and in the Implementation Plan and subsequently deliver into SEI's pre-production environment defined in the Implementation plan, an AI-powered fee calculation engine for Alt Fund Accounting (Stakeholder: Bryan Reeder) that will extract rates/terms/milestones from accounting system reports and Excel templates, and populate structured metadata repository, with version control and ability to store triggers in changes to base, rates, noted opt outs, with integration to workflow for approvals and QC ("In-Scope Processes") and eliminate time spent by SEI resources performing manual calculations of management, administrative incentive fees and carried interest (the "Deliverable"). The Solution will retrieve fee basis data systematically from Geneva/InvesTran/InvesTier reports into investor-level fee calculation engine eliminating manual population of templates, and will perform QC checks with transparency for user validation and approval, will integrate waterfall calculations in Anaplan, will automate uploaders to accounting engines and will deliver to existing client delivery platforms where clients can access fee calculation data as described in Appendix A to this schedule.
Accurate Dublin headcount is not available at the time of signing for this SOW, but the parties agree that a PCR is to be promptly executed to include Dublin in scope, with added headcount for impact adhering to the same phased delivery schedule.

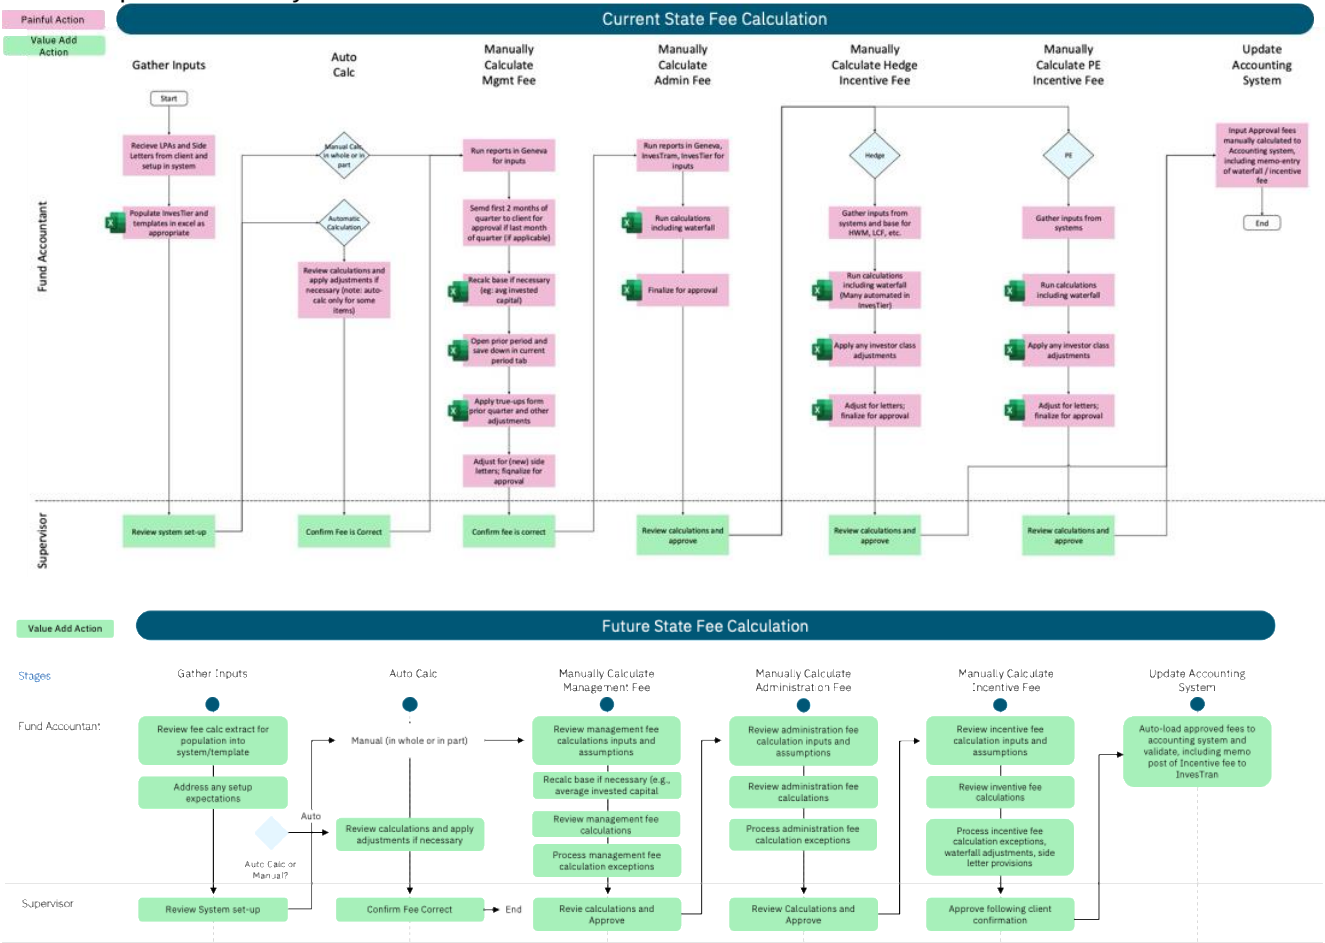

Agent Flow Architecture:

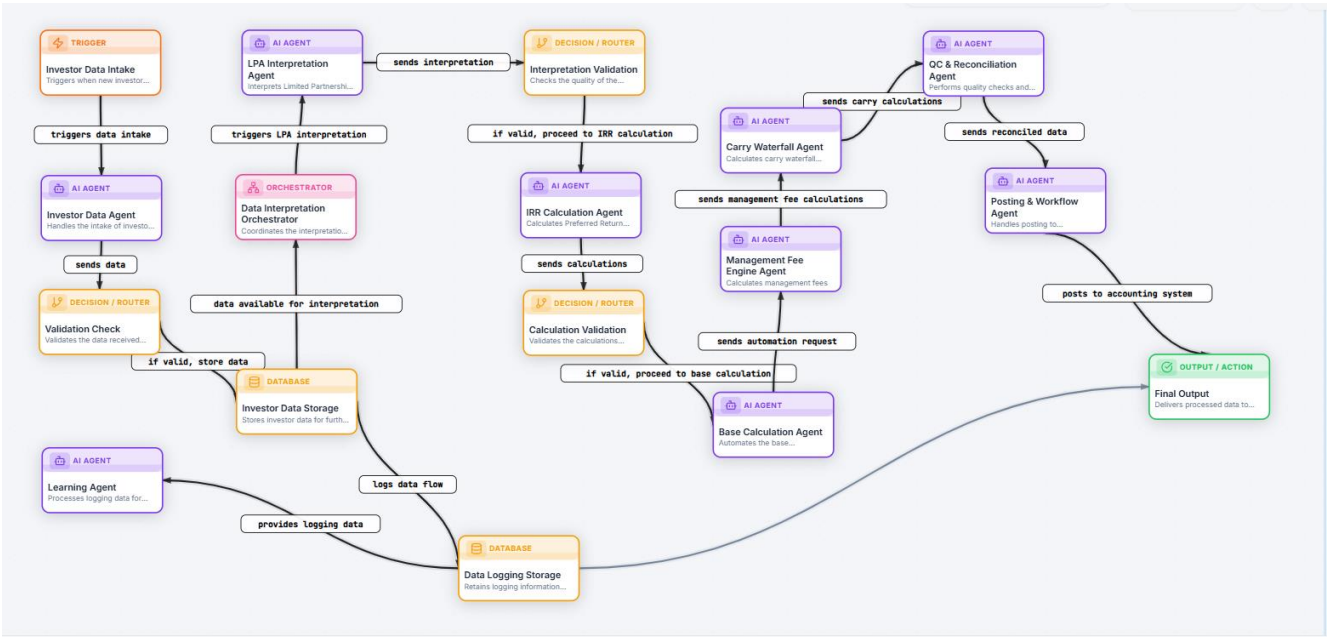

AI Physical Architecture:

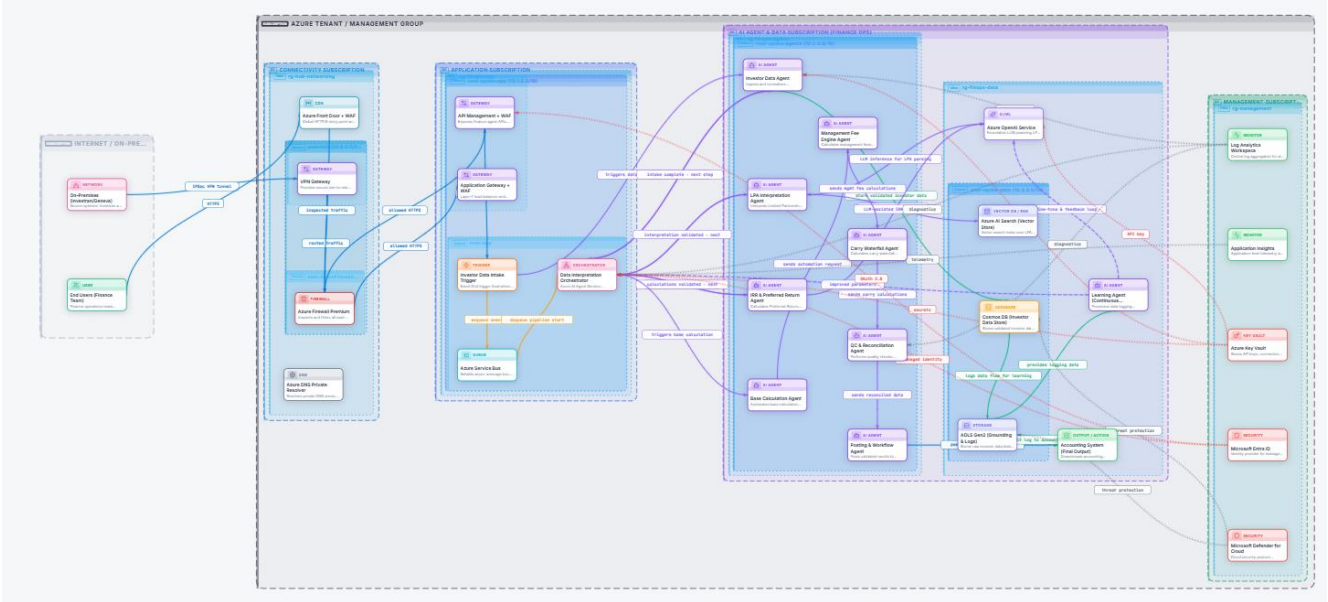

The solution will integrate with Anaplan for waterfall calculations for designated clients.
Vendor shall prepare and deliver the following documents to be reviewed and signed off by SEI:

1. **Analysis Documentation** – Process Definition documentation and User Stories in templates agreed with SEI
2. **Solution Design Artifacts** – Detailed solution architecture in templates agreed with SEI

- 3. **Test Documentation** – Test approach, test case and test data related documentation in templates agreed with SEI
- 4. **Solution Deployment Documentation** - Deployment Documentation in templates agreed with SEI
- 5. **Operational Documentation**– NA – Any updates to existing procedural documentation and change management related documentation will be handled by SEI inclusive of playbooks and operating guides. Vendor will provide requisite vendor developed solution documentation to support SEI with updating relevant Operational Documentation.

Pre-Production Delivery:

Pre-Production Environment: The environments used will be Dev, QA and UAT. Dev environment will be identified prior to development and QA, UAT environments will be identified prior to development completion during execution. This will be the environment where the code/automation will be moved, the systems of record validated for updates and sample automated fee calculations will be processed for validation by SEI.

Phase 1: Golden Data Set for Fee Calc; Management Fee Automation for Top 10 Clients including Agents for the 5 Value Concentrations

- Calculation Template Rollforward
- Report / Data Extraction from Accounting Systems
- Management Fee Calculation Engine
- Review / QC Agent
- Excel Output report Generator

Phase 2: Management Fee Automation for Next 12 Clients; Carried Interest Automation for Top 10 and Next 12 Clients

Phase 3: Incentive Fee Automation for Top 10, Next 12 and Remaining Clients; Management Fee Automation and Carried Interest Automation for Remaining Clients; Administrative Fee Automation for Top 10, Next 12 and Remaining Clients; Workflow Integration; Dashboard for Client Reporting

Note: It may not be practicable to automate calculations for all clients. There will always be some calculations that will require manual intervention

PHASE 1 — Golden Data Set for Fee Calculation and Management Fee Automation for Top 10 Clients

Scope: Management fee automation for Top 10 Clients, including agents for the 5 value concentrations:

- Calculation Template Rollforward
- Report / Data Extraction from Accounting Systems
- Management Fee Calculation Engine
- Review / QC Agent
- Excel Output Report Generator

Title	Description	Success Criteria
Data Extraction	Automate report generation from Geneva, Investran, Investier and extraction of data from reports for populating Excel for calculation of management, carried interest, incentive and administrative fees	Feature exists to generate reports from Geneva, Investran, and Investier and to extract data to populate Excel workbooks

Normalization	Normalize & filter data for populating Excel fee calculation templates	Feature exists to normalize data to populate Excel fee calculation templates / engines
Template Rollforward Agent	Automate preparation of fee calculation engine to ingest data and perform calculation for current period, invoking triggers as appropriate	Feature exists to prepare fee calculation engine for current period calculation
Management Fee Calc Engine	Automate management fee calculations for variations covering Top 10 Clients	Feature exists to calculate management fees
Management Fee Output Files	Generate management fee calculation output files in Excel to support client, audit and compliance requirements	Feature exists to generate management fee output files
Review / QC Agent	Perform automated QC of management fee calculations and provide evidentiary review content for reviewer approval	Feature exists to automate management fee QC and to display supporting content to facilitate reviewer approval

PHASE 2 — Extend Management Fee Automation and Deliver Carried Interest Calculation Automation

Scope: Management Fee Automation for Next 12 Clients; Carried Interest Automation for Top 10 and Next 12 Clients

Title	Description	Success Criteria
Management Fee Calc Engine Enhancements	Enhance management fee automation to meet unique needs of Next 12 Clients	Feature can be modified to calculate management fees for additional variations
Rework Agent	Diagnose potential source of calculation discrepancies and recommend remediation	Feature exists to automate rework tasks
Automated Upload	Automated journal entry posting into InvesTran / InvesTier, Geneva, leveraging existing uploader tools	Feature exists for automated journal entry to InvesTran and InvesTier, Geneva
Data Upload QC	Automated quality control check of data in InvesTran / InvesTier, Geneva following upload against input data	Feature exists to compare input data against corresponding upload data extracted from system with highlighted exceptions
Carried Interest Calc Engine	Automate carried interest calculations for variations covering Top 10 and Next 12 Clients	Feature exists to calculate carried interest
Carried Interest Output Files	Generation of carried interest calculation output files in Excel to support client, audit and compliance requirements	Feature exists to generate carried interest output files
Enhancements to Agents other than Calc Engine to support Carried Interest	Modify agents for carried interest scope for Top 10 and Next 12 Clients: - Calculation Template Rollforward - Report / Data Extraction from Accounting Systems	Features exist to support carried interest calculation across all agents / value concentrations

	• Review / QC Agent • Rework by Preparer • Record Entry Upon Approval (to Accounting Systems)	
--	---	--

PHASE 3 — Incentive and Administrative Fee Automation, Workflow and Dashboard

Scope: Incentive Fee Automation for all Clients; Management, Carried Interest and Incentive Fee Automation for Remaining Clients; Administrative Fee Automation for all Clients; Workflow Integration; Dashboard for Client Reporting

Title	Description	Success Criteria
Incentive Fee Calc Engine	Automation of incentive fee calculations for variations covering all Clients	Feature exists to calculate incentive fees
Incentive Fee Output Files	Generation of incentive fee calculation output files in Excel to support client, audit and compliance requirements	Feature exists to generate incentive fee output files
Administrative Fee Calc Engine	Automation of administrative fee calculations for variations covering all Clients	Feature exists to calculate administrative fees
Administrative Fee Output Files	Generation of administrative fee calculation output files in Excel to support client, audit and compliance requirements	Feature exists to generate administrative fee output files
Enhancements to Agents other than Calc Engine to support Incentive Fees and Administrative Fees	Modify agents for incentive and administrative fee scope for all Clients: • Calculation Template Rollforward • Report / Data Extraction from Accounting Systems • Review / QC Agent • Rework by Preparer • Record Entry Upon Approval (to Accounting Systems)	Features exist to support incentive and administrative fee calculations across all agents / value concentrations
Automated Invoice Generation	Automated draft invoice generation for administrative fees	Feature exists for automated administrative fee invoice generation
Workflow Integration	Integration with Jira / ServiceNow for fee input capture, client fee communication / approvals, internal tracking	Automated leverage of workflow
Client Reporting Dashboard	Dashboard to provide clients with transparency on fee calculations, both status and supporting content	Feature exists to provide entitled clients with self-service access to fee calculation status and detail

Acceptance Test:

The UAT will be performed with the goal of measuring and validating the following on a phase-by-phase basis

Phase 1

- Accuracy and completeness of data extracted from systems
- Time elapsed for automated extraction of data from systems
- Accuracy of auto-calculated management fees
- Accuracy of auto-generated management fee output files
- Time elapsed for auto-calculation of management fees

Phase 2

- Accuracy of auto-calculated management fees for added scope
- Accuracy of auto-generated management fee output files for added scope
- Time elapsed for auto-calculation of management fees for added scope
- Accuracy of auto-calculated carried Interest
- Accuracy of auto-generated carried interest output files
- Time elapsed for auto-calculation of carried interest

Phase 3

- Accuracy of auto-calculated incentive fees
- Accuracy of auto-generated incentive fee output files
- Time elapsed for auto-calculation of incentive fees
- Accuracy of auto-calculated administrative fees
- Accuracy of auto-generated administrative fee output files
- Time elapsed for auto-calculation of administrative fees
- Accuracy of workflow integration for fee calculation inputs, client communication / approvals and for internal tracking
- Accuracy of automated billing system uploads of administrative fees
- Accuracy of information on Client Reporting Dashboard and performance within market standards

Acceptance Criteria for each Deliverable:

1. Quality of output is not less than the current quality (error rates)
2. Processing time reduction of 25% or higher

Production Delivery:

Dependencies and SEI Internal Requirements

1. *Dependencies*

Dependency	Description	Responsible Party	Estimated Time Period
<i>Anaplan Data</i>	<i>Two-way transfer of data for waterfall calc for small number of funds (~100)</i>	<i>SEI</i>	<i>Phase 2</i>
<i>Geneva Data</i>	<i>Access to data as input for fee calculations and use of uploader for approved entries</i>	<i>SEI</i>	<i>Phase 1</i>

<i>InvesTran Data</i>	<i>Access to data as input for fee calculations and use of uploader for approved entries</i>	<i>SEI</i>	<i>Phase 1</i>
<i>InvesTier Data</i>	<i>Access to data as input for fee calculations and use of uploader for approved entries</i>	<i>SEI</i>	<i>Phase 1</i>
<i>Jira Integration</i>	<i>Two-way integration for content extraction, status updates and ticket creation</i>	<i>IBM</i>	<i>Phase 3</i>
<i>Corporate Billing Data</i>	<i>Use of uploader for administrative fee calculations and bill generator automation</i>	<i>SEI</i>	<i>Phase 3</i>

2. SEI Internal Requirements and Expected Timing

Internal Process	Internal Stakeholder	Responsible Party	Estimated Time Period
<i>SEI Internal Procedures with team-by-team considerations</i>	<i>Bryan Reeder</i>	<i>Jim Sinclair</i>	<i>Prior to each phase go-live</i>
<i>Any client approvals for use of AI on data</i>	<i>Bryan Reeder</i>	<i>Jim Sinclair</i>	<i>Phase 1</i>
<i>Audit trail / output templates required by clients and for SEI compliance</i>	<i>Bryan Reeder</i>	<i>Jim Sinclair</i>	<i>Phase 1</i>
<i>Infrastructure set-up for development, UAT and production environments to build and deploy automations</i>	<i>Brad Landis</i>	<i>Zach Womack</i>	<i>Prior to commencement of respective project phases</i>

Schedule 2 Fees

1. Constant Costs

The parties agree the following costs have been validated for calculation of both the SOW Transformation Value and the Gainshare Fees:

a. Annual In-Scope Constant Cost/FTE

Role	US	Dublin	Offshore
Fund Accountant I / Ops Analyst I	\$ 65,000	NA	NA
Fund Accountant II / Ops Analyst II	\$ 73,000	NA	NA
Supervisor	\$ 93,000	NA	NA
Sr. Supervisor	\$ 108,000	NA	NA
Asst. Manager	\$ 120,000	NA	NA
Manager I	\$ 142,000	NA	NA
Sr. Manager / Manager II	\$ 159,000	NA	NA
Assistant Director	\$ 183,000	NA	NA

Current Total In-Scope Annual Spend

Role	Annual FTE Capacity (US)	Average Cost US	Annual FTE Capacity (Dublin)	Average Cost Dublin	Annual FTE Capacity (India)	Average Cost India	Total Cost
Analyst	22.5	\$68,550	TBC		N/A	-	\$ 1,542,375
Supervisor	19.65	\$107,205	TBC		N/A	-	\$ 2,106,581
Manager	5.89	\$164,373	TBC		N/A	-	\$ 968,154
Total							\$ 4,617,110

b. Total Value Creation

- i) Increased Efficiency (reduction in processing time): Expected processing time reduction of 55% delivering \$ 2,539,411 in annual savings.

2. SEI Internal Enablement Costs

The parties hereby agree that the internal SEI resource commitments and third-party expenditure required to procure under this SOW are expected to be a total of \$40,000 which includes the following components:

- Annual Technology and Infrastructure Cost - \$40,000 which includes but not limited to the following components:
 - 1. LLM Tokens
 - 2. Container Apps
 - 3. Storage (Blob and RDB)

3. SOW Transformation Value Calculation Methodology

For the purposes of this SOW, the following terms shall have the following meanings:

“Total Annual Spend Reduction” shall mean the Current Total In-Scope Annual Spend less the End State Total In-Scope Annual Spend set forth in Schedule 3.

“SOW Transformation Value “- The Total Annual Spend Reduction plus the Total Value Creation less the SEI Enablement Costs set forth below.

“End State Annual Spend” – means the sum of (the On-Shore Target In-Scope FTE for each Role set forth in Schedule 3 multiplied by the On-Shore Total In-Scope Annual Constant Cost/FTE for the applicable role) plus the sum of (the Off-Shore Target In-Scope FTE by Role set forth in Schedule 3 multiplied by the Off-Shore Total In-Scope Annual Constant Cost/FTE for the applicable role.

4. SOW Transformation Value

The parties hereby agree the Transformation Value for this SOW is \$ 2,499,411 (the “**SOW Transformation Value**”).

SOW Value Creation	\$ 2,539,411
SEI Internal Enablement Costs (12 months)	\$ 40,000
SOW Transformation Value	\$ 2,499,411

5. Gainshare Fees

SEI hereby agrees to pay Vendor fees (the “Gainshare Fees”) estimated at \$749,823 for, and Vendor agrees to perform, the Services set forth in Schedule 1. The estimated Gainshare Fees are calculated at 30% of the SOW Transformation Value for all phases listed in Section 6. Transformation Value and Gainshare Fees will be memorialized at Delivery Completion milestone and 70% of the Gainshare Fees will be paid to Vendor (“Initial Fee”). Actual Transformation value and Gainshare Fees will be memorialized at Validation milestone to reflect actual SOW Transformation Value and any remaining Gainshare Fees will be paid to the vendor (“Remaining Fee”).

		Estimated Transformation Value	Demonstrated at Delivery Completion Milestone	Actual at Validation Milestone
Phase 1	Transformation Value	\$ 358,791	TBC	TBC
	Gainshare Fees	\$ 107,637	TBC	TBC
Phase 2	Transformation Value	\$ 1,013,688	TBC	TBC
	Gainshare Fees	\$ 304,106	TBC	TBC

Phase 3	Transformation Value	\$ 1,126,932	TBC	TBC
	Gainshare Fees	\$ 338,080	TBC	TBC
Total	Transformation Value	\$ 2,499,411	TBC	TBC
	Gainshare Fees	\$ 749,823	TBC	TBC

TBC = To Be Calculated

2 Payment Schedule

The parties agree that the Gainshare Fees shall be paid based on the payment schedule found in the table below:

	Estimated Initial Fee	Anticipated date	Payment	Estimated Fee	Remaining	Anticipated date	Payment
Phase 1 (Golden Data Set for Fee Calc and Mgmt Fee Automation for Top 10 Clients, excluding posting)	\$75,346	9/11/2026		\$32,291		12/9/2026	
Phase 2 (Extend Mgmt Fee Automation and Deliver Carried Interest Calc Automation)	\$212,874	11/20/2026		\$91,232		2/18/2027	
Phase 3 (Incentive and Administrative Fee Automation, Workflow and Dashboard)	\$236,656	2/19/2027		\$101,424		5/20/2027	
TOTAL	\$ 524,876			\$224,947			

The deployment will follow a 3-phased approach as referenced in Schedule 1. The initial fees were calculated based on 14% of total effort being addressed in Phase 1, 41% in Phase 2, 45% in Phase 3.

Client Name	Category	Phase
Client L	Top 10	Phases 1-3
Client M	Top 10	Phases 1-3
Client N	Top 10	Phases 1-3
Client O	Top 10	Phases 1-3
Client P	Top 10	Phases 1-3
Client Q	Top 10	Phases 1-3
Client R	Top 10	Phases 1-3
Client S	Top 10	Phases 1-3
Client T	Top 10	Phases 1-3
Client A	Top 10	Phases 1-3
Client E	Next 12	Phases 2-3
Client U	Next 12	Phases 2-3
Client F	Next 12	Phases 2-3
Client J	Next 12	Phases 2-3
Client V	Next 12	Phases 2-3

Client W	Next 12	Phases 2-3
Client X	Next 12	Phases 2-3
Client H	Next 12	Phases 2-3
Client Y	Next 12	Phases 2-3
Client I	Next 12	Phases 2-3
Client Z	Next 12	Phases 2-3
Client A1	Next 12	Phases 2-3
Other Clients (approximately 120)	Other Clients	Phase 3

Note: It may not be practicable to automate calculations for all clients. There will always be some calculations that will require manual intervention

Schedule 3 Measurement Metrics and Acceptance Testing

Measurement Metrics and Acceptance Criteria

The parties hereby agree that the following metrics will be the applicable measurement metrics (the “**Measurement Metrics**”) for measurement purposes and demonstration that the Deliverable achieves the Target Measurement Metrics (as defined below) shall constitute the acceptance criteria and the criteria for Validation (the “**Acceptance Criteria**”). For the purposes of this SOW UC-19, “Onshore” shall mean the US and Dublin and “Offshore” shall mean India.

Measurement Metrics

Processing Time – The amount of time spent performing the In-Scope Process in current state vs future state.

Separate performance testing is not planned at this time. During UAT it will be determined that the solution does not cause any degradation in the performance of existing applications.

Baseline Measurement Metrics

The parties agree the following Measurement Metrics will be used as the Baseline Measurement Metrics and will be the basis for calculation of both the SOW Transformation Value and the Gainshare Fees. These figures, which exclude initial set-up, were provided by SEI and are subject to validation with a sampling jointly observed by IBM and SEI

- a. Management Fees
 - i. InvesTran “Easy” 3.61 Hours/Fund Average Per Occurrence
 - ii. InvesTran “Complex” 5.77 Hours/Fund Average Per Occurrence
 - iii. InvesTier “Easy” 3.28 Hours/Fund Average Per Occurrence
 - iv. InvesTier “Complex” 3.09 Hours/Fund Average Per Occurrence
 - v. InvesTier/Investran “Automated” 0.25 Hours/Fund Average Per Occurrence

The InvesTier management fee calculation process includes a subset of fee calculations that are fully automated within the system, and accordingly, do not require the full extent of automation

efforts by the Vendor. Similar automated calculations may also exist within Investran that follow this same premise. Such automated calculations are reflected in the Current Total In-Scope Annual Spend.

The specific population of such automated calculations shall be further defined and mutually agreed upon by SEI and the Vendor, and documented in an appendix to be added to this Statement of Work. This definition will be established as part of the Solution Design documentation and subsequently validated through the Test Approach, Test Data, and Test Case Planning activities, as set forth in this Statement of Work.

- b. Carried Interest
 - i. Realized Macro (no Anaplan) 4.07 Hours/Fund Average Per Occurrence
 - ii. Realized No Macro (no Anaplan) 6.17 Hours/Fund Average Per Occurrence
 - iii. Unrealized Macro (no Anaplan) 3.56 Hours/Fund Average Per Occurrence
 - iv. Unrealized No Macro (no Anaplan) 5.9 Hours/Fund Average Per Occurrence
- c. Admin Fees
 - i. 9.68 Hours/Client Per Occurrence (SEI and IBM agree that it may be necessary to revisit this item if it is determined that integration to the Advantage Fee system is not in scope)
- d. Manual interface with workflow or e-mail effort as an alternative is integrated in the tasks above. Validation may be performed to measure the baseline effort separately

Target Measurement Metrics

- a. Target efficiency improvement is 55% across all in-scope tasks
- b. Dashboard / reporting enhancement shall have a value assigned for experience improvement

Testing Criteria/ Methodology

The parties hereby agree that for the purpose of the Measurement Metrics for calculation of BAU Measurement Metrics and Acceptance Testing, the following testing parameters shall apply.

Sample Criteria

1. Sample size - 80 requests
2. Samples will include 80 in proportions representative of the Production environment
3. Samples will include 80 examples from representative clients for respective implementation phases
4. Ability to validate all 80
5. Appropriate test environments available to validate E2E workflow (as required)

Notwithstanding the foregoing, the sample size may be reasonably adjusted by mutual agreement of the parties to ensure sufficient representation and coverage of applicable variations and deviations (including, without limitation, fee base types). Any such adjustment shall be made for the purpose of ensuring that the defined population of fee calculation types is adequately tested and appropriately reflected within the scope and capabilities of the solution developed by the Vendor.

Quality Testing

- a. Agents route to next phase when passing approved confidence ratio and offboard when not

- b. Data entry into InvesTran and InvesTier , Geneva is complete and accurate

Each fee type within the scope of this Statement of Work may include variations and deviations (including, without limitation, fee base types) that must be incorporated into the solution to be developed by the Vendor.

The specific population of such deviations shall be further defined and mutually agreed upon by SEI and the Vendor, and documented in an appendix to be added to this Statement of Work.

Such defined population will be used by SEI and the Vendor during the Validation Period to confirm the extent to which the overall population is addressed by, and derives benefit from, the solution developed by the Vendor, and to identify any portion of the population not supported or otherwise out of scope of the solution.

Processing Time testing

- a. Initial enablement of users to interact with the automation at a comfortable level

4 rounds of testing will be performed (average of 20 requests each round) – average processing time will be calculated based on the time taken to execute the testing with IBM being side by side with SEI

Schedule 4 Termination Rights and Fees

In the event SEI elects to terminate this SOW for convenience before the end of the SOW Initial Term, SEI shall pay Vendor a termination fee not to exceed \$700,000, prorated to reflect the portion of the Services completed as of the effective date of termination and the portion of the Implementation Plan elapsed as of such date. The applicable termination fee shall be calculated by multiplying \$700,000 by a fraction, the numerator of which is the weighted percentage of work actually completed under the Implementation Plan as of the effective date of termination and the denominator of which is one hundred percent (100%); provided that such amount shall not exceed the amount that would be payable based on the percentage of the Implementation Plan period elapsed as of the effective date of termination. Vendor shall provide reasonable supporting documentation for the work completed and the calculation of the prorated termination fee.

Schedule 5
Technology Tools and Existing IP

19. Pre-Existing IP:

- a. SEI: None
- b. Vendor: None

20. Tech Tools:

This project will leverage the following foundational technology platforms:

Category	Component	Requirement / Description
Application Layer	Azure App Service	Hosts web UI and REST APIs
	REST APIs	Enables integration with external and internal systems
	UI (Composer)	Used for configuration, monitoring, and human review
Compute & Orchestration	Azure Container Apps	Runs DocuFlow backend and multi-agent orchestration
	Azure Function Apps	Executes modular processing and integrations
	Agent Framework	Coordinates extraction, validation, and business rule agents
Data & Storage	Azure Blob Storage	Stores raw documents, outputs, and intermediate files
	Azure Storage Accounts	Supports orchestration state, logs, and training datasets
	Cosmos DB (Mongo API)	Stores prompts, configuration, and ontology definitions
	Azure AI Search (Vector DB)	Provides long-term memory and semantic search over documents
AI Services	Azure Document Intelligence	OCR, layout extraction, prebuilt document models
	Azure OpenAI	Extraction, enrichment, validation, and formatting using LLMs
	Cognitive Services	Additional NLP and AI capabilities
Security & Governance	Identity & Access	Azure Entra ID (RBAC) for user and system access
	Compliance	Azure Policy for governance and regulatory enforcement
	Auditability	Tracks corrections, validation, and processing actions
Resiliency	High Availability	Multi-region failover and resilient processing pipeline
	Data Persistence	Stores intermediate states and logs for recovery
Deployment	Environments	Dev, Test, UAT, Prod with isolated resources
	Platform Model	Azure PaaS-based, scalable, event-driven architecture

	DevOps	GitHub (or other repo platform)
--	--------	---------------------------------

Appendix A Implementation Plan (the “Implementation Plan”)

A detailed Implementation Plan and implementation schedule; with time periods allocated to each phase; each Implementation Plan must include the anticipated Opportunity Go-Live date, and Validation Period.

★ Milestone

Phase	May-26 Month 1	Jun-26 Month 2	Jul-26 Month 3	Aug-26 Month 4	Sep-26 Month 5	Oct-26 Month 6	Nov-26 Month 7	Dec-26 Month 8	Jan-27 Month 9	Feb-27 Month 10	Mar-27 Month 11	Apr-27 Month 12	May-27 Month 13
Phase I (Golden Data Set for Fee Calc and Mgmt Fee Automation for Top 10 Clients)		Planning & Automation Build		UAT ★ Deploy ★	Validation Period								
Phase II (Extend Mgmt Fee Automation and Deliver Carried Interest Calc Automation)				Planning & Automation Build		UAT ★ Deploy ★	Validation Period			★			
Phase III (Incentive and Administrative Fee Automation, Workflow and Dashboard)							Planning & Automation Build		UAT ★ Deploy ★	Validation Period			★

Step	Period/Scheduled Completion Date	Owner
Phase 1 – Golden Data Set for Fee Calculation and Management Fee Automation for Top 10 Clients		
User Stories + related Process Definition documentation completion	6/8/2026	IBM
Solution Design documentation and validation	6/15/2026	IBM
Test Approach, Test Data and Test Case Planning	6/22/2026	IBM
Build and Configure	8/21/2026	IBM
Move to Pre-Production	8/14/2026	IBM
UAT Completion	9/4/2026	IBM / SEI
Production Change Control completion	9/11/2026	SEI
Production Deployment	9/11/2026	SEI
Hypercare/Post-Implementation Support	9/25/2026	IBM
Validation Period	12/9/2026	SEI
Phase 2 – Extend Management Fee Automation and Deliver Carried Interest Calculation Automation		
User Stories + related Process Definition documentation completion	8/28/2026	IBM

Solution Design documentation and validation	9/4/2026	IBM
Test Approach, Test Data and Test Case Planning	9/11/2026	IBM
Build and Configure	10/23/2026	IBM
Move to Pre-Production	10/16/2026	IBM
UAT completion	11/13/2026	IBM/SEI
Production Change Control completion	11/20/2026	SEI
Production Deployment	11/20/2026	SEI
Hypercare/Post-Implementation Support	12/4/2026	IBM
Validation Period	2/18/2027	SEI
Phase 3 – Incentive and Administrative Fee Automation, Workflow and Dashboard		
User Stories + related Process Definition documentation completion	11/13/2026	IBM
Solution Design documentation and validation	11/20/2026	IBM
Test Approach, Test Data and Test Case Planning	11/27/2026	IBM
Build and Configure	1/22/2027	IBM
Move to Pre-Production	1/15/2027	IBM
UAT completion	2/12/2027	IBM/SEI
Production Change Control Completion	2/19/2027	SEI
Production Deployment	2/19/2027	SEI
Hypercare/Post-Implementation Support	3/5/2027	IBM
Validation Period	5/20/2027	SEI

Sample Documentation Request Requirements:

SEI will use commercially reasonable efforts to provide sample data according to the requirements and timelines mentioned in the table below, for Vendor to be able to adequately perform the anticipated Build and Configure activities in the Implementation Plan. The sample documentation will be scrubbed of all personally identifiable information according to SEI requirements.

Client	Fund Count	Date Required
Top 10 (All)	1 Fund per Client (10 Funds Total)	6/26/2026
Client N Client O Client S Client T	9 Funds per Client (36 Funds Total)	7/2/2026
Client L Client P	9 Funds per Client (18 Funds Total)	7/9/2026
Client M Client Q Client R Client A	9 Funds per Client (36 Funds Total)	7/16/2026
